


ID	Task Mode	Task Name	Work	Duration	Start	Finish	Predec	May 31, '20							Jun 7, '20							Jun 14, '20							Jun 21, '20						
								T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
1		<b>Hall D Operations Resumption</b>	<b>424.8 hrs</b>	<b>25.13 days</b>	<b>Mon 5/25/20</b>	<b>Mon 6/29/20</b>																													
2		Administration procedures & discussions	16 hrs	1 day	Mon 5/25/20	Mon 5/25/20		Stevens, Foyles																											
3		<b>Detectors (Reference Checklists)</b>	<b>64.72 hrs</b>	<b>25.13 days</b>	<b>Mon 5/25/20</b>	<b>Mon 6/29/20</b>																													
4		Stevens -Oversite Supervision	40 hrs	5 days	Mon 5/25/20	Fri 5/29/20		Stevens																											
5		Turn on Microscope fan	0.24 hrs	0.03 days	Tue 5/26/20	Tue 5/26/20		Foyles																											
6		Turn on CDC Blowers	2 hrs	0.25 days	Tue 5/26/20	Tue 5/26/20		Foyles																											
7		Adjust BCal N2 purge	0.24 hrs	0.03 days	Tue 5/26/20	Tue 5/26/20		Foyles																											
8		ComCal N2 Purge	0.24 hrs	0.03 days	Tue 5/26/20	Tue 5/26/20		Foyles																											
9		ComCal - Reactivate Chiller	4 hrs	0.5 days	Tue 5/26/20	Tue 5/26/20		Foyles																											
10		Bcal Chiller US - Use Procedure	6 hrs	0.75 days	Wed 5/27/20	Wed 5/27/20		Foyles																											
11		Bcal Chiller DS - Use Procedure	6 hrs	0.75 days	Thu 5/28/20	Thu 5/28/20		Foyles																											
12		FDC Chillers - Use Procedures	4 hrs	0.5 days	Fri 5/29/20	Fri 5/29/20		Foyles																											
13		Re-establish Detectors Gas Sup	2 hrs	0.13 days	Mon 6/29/20	Mon 6/29/20																													
14		<b>DIRC</b>	<b>72 hrs</b>	<b>2 days</b>	<b>Mon 6/1/20</b>	<b>Tue 6/2/20</b>																													
15		<b>Spiegel - Oversight Supervision</b>	<b>72 hrs</b>	<b>2 days</b>	<b>Mon 6/1/20</b>	<b>Tue 6/2/20</b>	4																												
16		Users Group Checklists	16 hrs	2 days	Mon 6/1/20	Tue 6/2/20		Users Group																											
17		Readjust N2 purge	2 hrs	0.25 days	Mon 6/1/20	Mon 6/1/20		Spiegel																											
18		Restart Water Cart	3.04 hrs	0.38 days	Mon 6/1/20	Mon 6/1/20		Blackburn																											
19		Add water when necessary	8 hrs	1 day	Mon 6/1/20	Mon 6/1/20		Blackburn																											
20		Refill Both Optical Boxes	16 hrs	2 days	Mon 6/1/20	Tue 6/2/20		Blackburn																											
21		Replace water filters & UV L	2 hrs	0.25 days	Tue 6/2/20	Tue 6/2/20	19	Blackburn																											
22		Obtain Water Samples	0.48 hrs	0.06 days	Tue 6/2/20	Tue 6/2/20		Blackburn																											
23		Secure release by RADCON	8 hrs	1 day	Tue 6/2/20	Tue 6/2/20		Blackburn																											
24		Turn on Tagger NMR Probe	0.48 hrs	0.06 days	Tue 6/2/20	Tue 6/2/20		Whitlatch																											
25		<b>Vacuum Systems</b>	<b>39 hrs</b>	<b>3 days</b>	<b>Wed 6/3/20</b>	<b>Fri 6/5/20</b>																													
26		<b>Spiegel - Oversight Supervision</b>	<b>39 hrs</b>	<b>3 days</b>	<b>Wed 6/3/20</b>	<b>Fri 6/5/20</b>	15	Blackburn																											
27		Verify Goni. Valves Operation w/ MCC	2 hrs	0.25 days	Wed 6/3/20	Wed 6/3/20		Blackburn																											
28		Verify Tagger Valve Operation w/MCC	2 hrs	0.25 days	Wed 6/3/20	Wed 6/3/20		Blackburn																											
29		Verify 10" Beam Pipe Tag/Coll. Cave Valve	2 hrs	0.25 days	Wed 6/3/20	Wed 6/3/20		Blackburn																											
30		Turn on Collimator Cave Vacuum Pumps w/	4 hrs	0.5 days	Wed 6/3/20	Wed 6/3/20		Blackburn																											
31		Turn on US platform Beamline Vacuum Pumps	4 hrs	0.5 days	Thu 6/4/20	Thu 6/4/20		Blackburn																											
32		Turn on DS FCal Platform Dump Pipe w/ Procedure	1 hr	0.13 days	Fri 6/5/20	Fri 6/5/20		Spiegel																											
33		<b>Power Supply Checklists</b>	<b>101.08 hrs</b>	<b>5 days</b>	<b>Mon 6/8/20</b>	<b>Fri 6/12/20</b>																													

Project: Project Hall D Resumpt  
Date: Tue 5/19/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

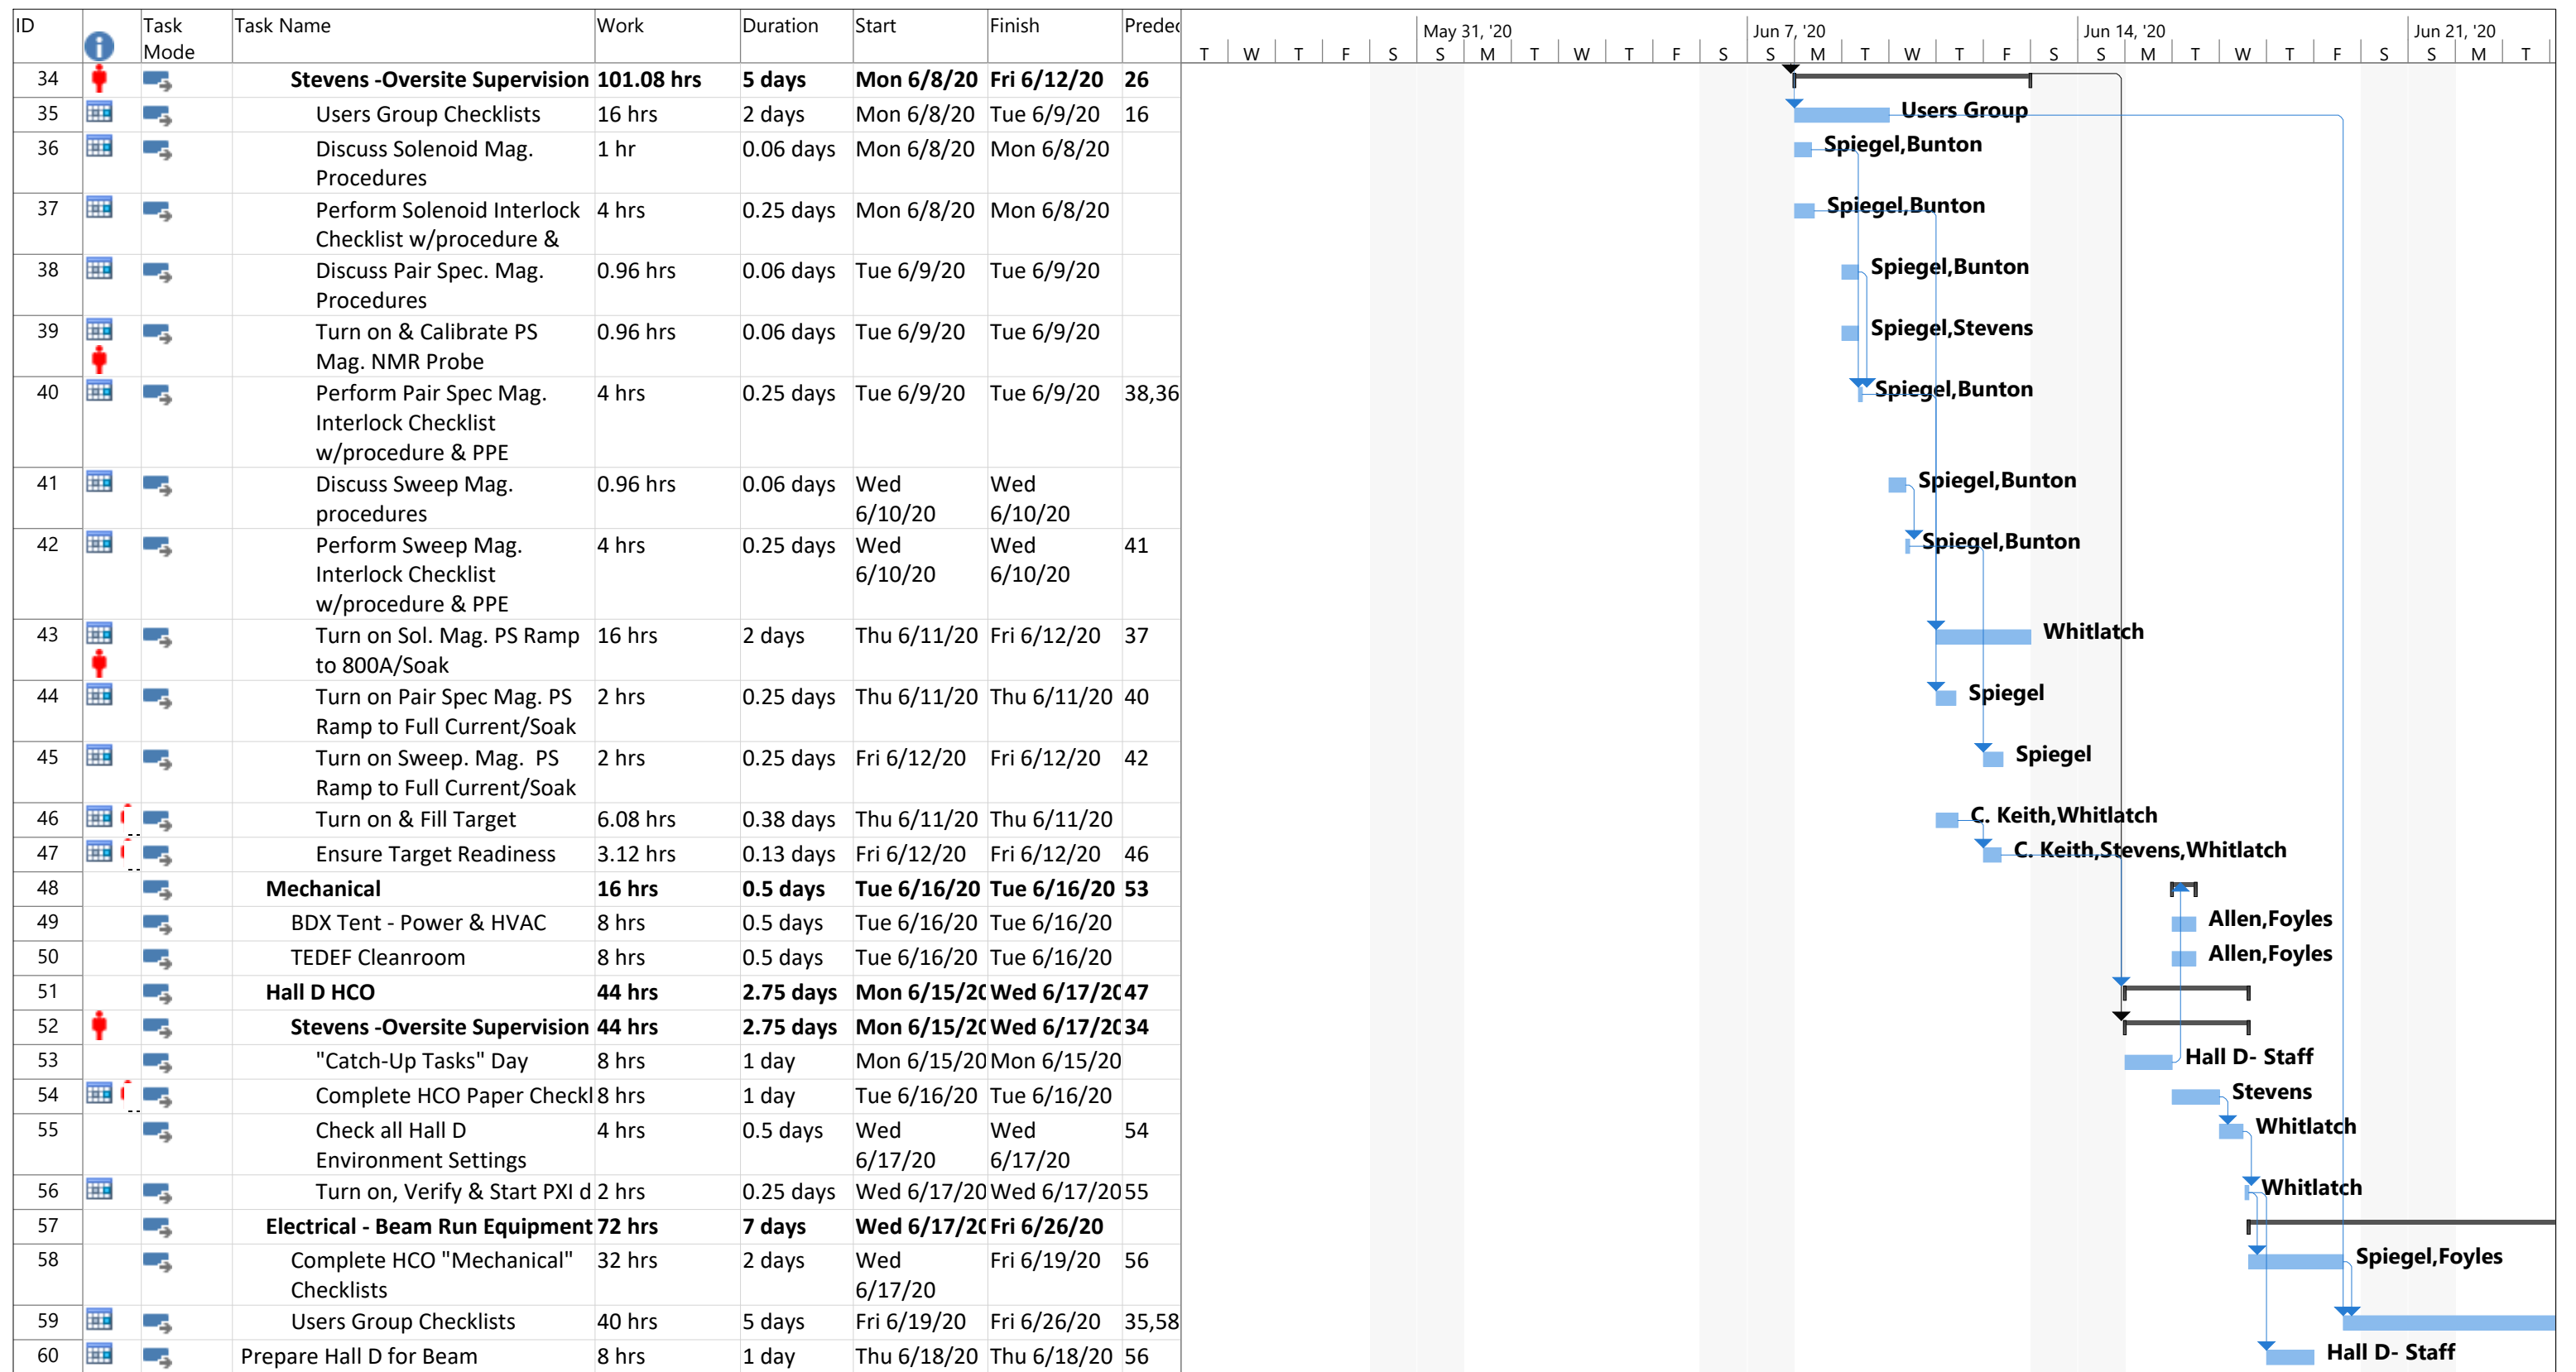

Project: Project Hall D Resumpt  
Date: Tue 5/19/20

Task	Project Summary	Manual Task	Start-only	Deadline	Progress
Split	Inactive Task	Duration-only	Finish-only	Manual Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks		
Summary	Inactive Summary	Manual Summary	External Milestone		
